

Record of Protective Relay Test Results

Performed By:

CEMIRT

Base:	Dyess AFB TX	Relay:	Multifunction
Substation:	Alpha	Device:	Microprocessor
Feeder:	A2 West Housing	Manufacturer:	GE
Tested By:	Mr. Willet/SSgt Miron	Inst. Bklt:	GEK-86132
Date Tested:	08/24/2016	Relay Test Set:	Megger MPRT 8430

Setting:	Value:	Description:
RID	2	CEMIRT Relay Identifier
Circuit Designator	A2	Circuit Identifier
Model	SR 760	MFG Model Type
Serial Number	B702723	MFG Serial Number
MFG Date	2008	Manufacturers Build Date
Phase Time OC1		
Pickup	0.30	Pickup Current x5
Curve	Extremely Inverse	Time Curve Shape
Multiplier	1.20	Time Curve Multiplier
Neutral Time OC1		
Pickup	0.15	Pickup Current x5
Curve	Extremely Inverse	Time Overcurrent Curve
Multiplier	1.20	Time Curve Multiplier

Relay 2: A-Phase Pickup Test

Actual Pickup (Amps)	Expected Pickup (Amps)	Min Range (Amps)	Max Range (Amps)	Pass/Fail (Result)
1.49	1.50	1.42	1.58	Pass

Relay 2: B-Phase Pickup Test

Actual Pickup (Amps)	Expected Pickup (Amps)	Min Range (Amps)	Max Range (Amps)	Pass/Fail (Result)
1.50	1.50	1.42	1.58	Pass

Relay 2: C-Phase Pickup Test

Actual Pickup (Amps)	Expected Pickup (Amps)	Min Range (Amps)	Max Range (Amps)	Pass/Fail (Result)
1.50	1.50	1.42	1.58	Pass


Record of Protective Relay Test Results

Performed By:

CEMIRT

Base:	Dyess AFB TX	Relay:	Multifunction
Substation:	Alpha	Device:	Microprocessor
Feeder:	A2 West Housing	Manufacturer:	GE
Tested By:	Mr. Willet/SSgt Miron	Inst. Bklt:	GEK-86132
Date Tested:	08/24/2016	Relay Test Set:	Megger MPRT 8430

Relay 2: A-Phase Time Overcurrent Test

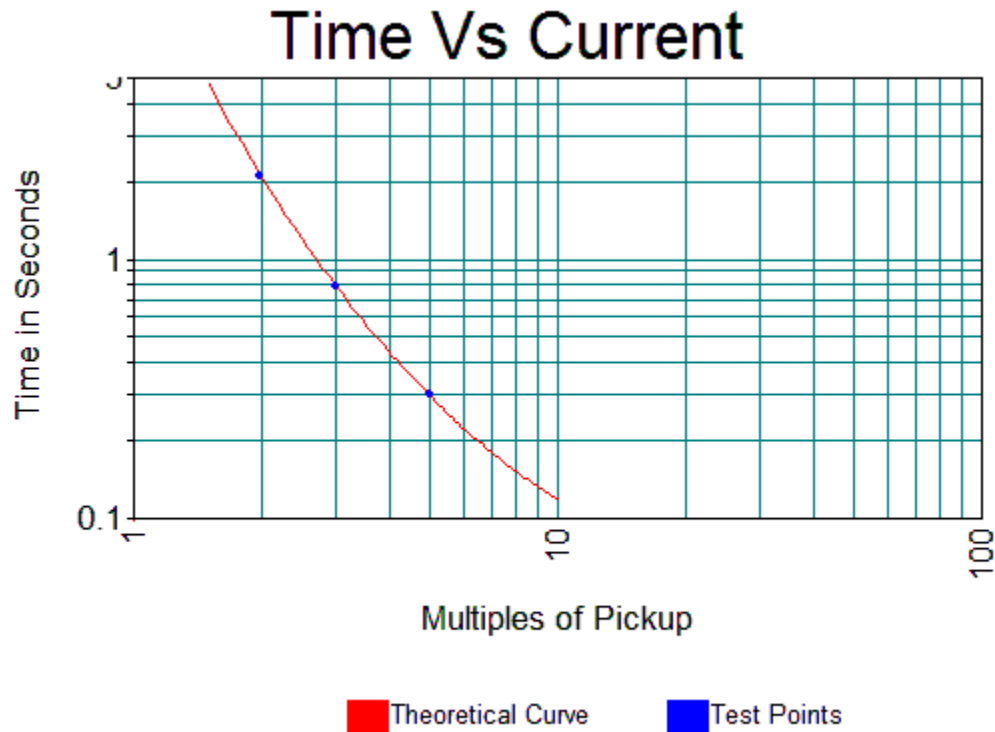

Multiple (X Tap)	Actual Time (Seconds)	Expected Time (Seconds)	Min Range (Seconds)	Max Range (Seconds)	Pass/Fail (Results)
2.00	2.08	2.09	1.99	2.20	Pass
3.00	0.78	0.79	0.75	0.83	Pass
5.00	0.30	0.30	0.28	0.31	Pass


Record of Protective Relay Test Results

Performed By:

CEMIRT

Base:	Dyess AFB TX	Relay:	Multifunction
Substation:	Alpha	Device:	Microprocessor
Feeder:	A2 West Housing	Manufacturer:	GE
Tested By:	Mr. Willet/SSgt Miron	Inst. Bklt:	GEK-86132
Date Tested:	08/24/2016	Relay Test Set:	Megger MPRT 8430

Relay 2: B-Phase Time Overcurrent Test

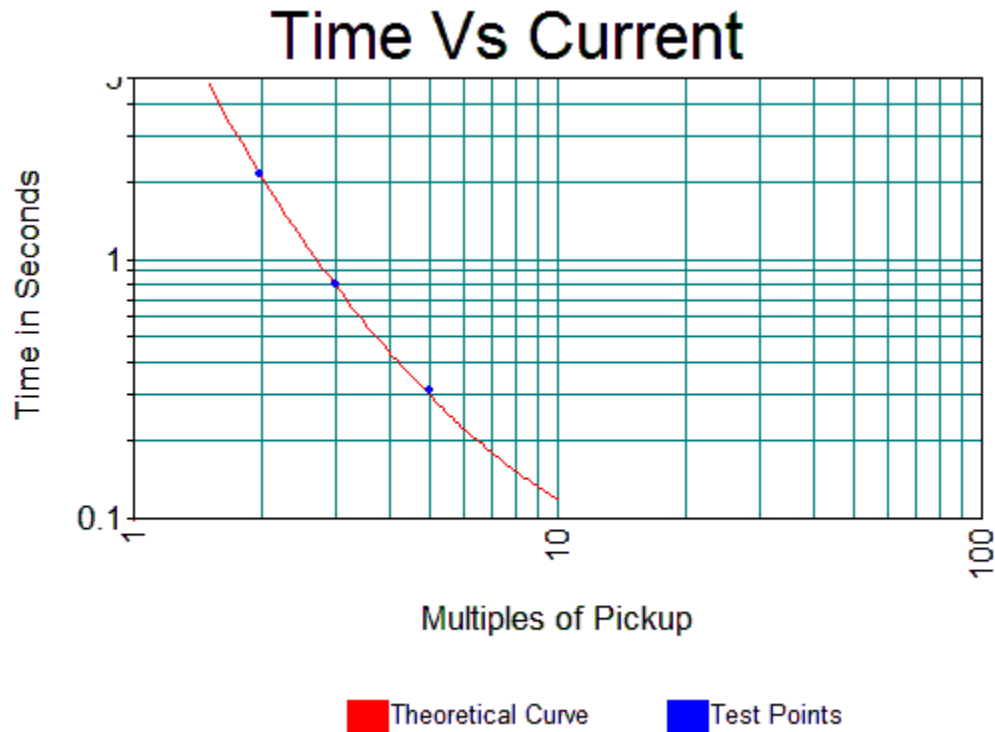

Multiple (X Tap)	Actual Time (Seconds)	Expected Time (Seconds)	Min Range (Seconds)	Max Range (Seconds)	Pass/Fail (Results)
2.00	2.11	2.09	1.99	2.20	Pass
3.00	0.80	0.79	0.75	0.83	Pass
5.00	0.31	0.30	0.28	0.31	Pass


Record of Protective Relay Test Results

Performed By:

CEMIRT

Base:	Dyess AFB TX	Relay:	Multifunction
Substation:	Alpha	Device:	Microprocessor
Feeder:	A2 West Housing	Manufacturer:	GE
Tested By:	Mr. Willet/SSgt Miron	Inst. Bklt:	GEK-86132
Date Tested:	08/24/2016	Relay Test Set:	Megger MPRT 8430

Relay 2: C-Phase Time Overcurrent Test

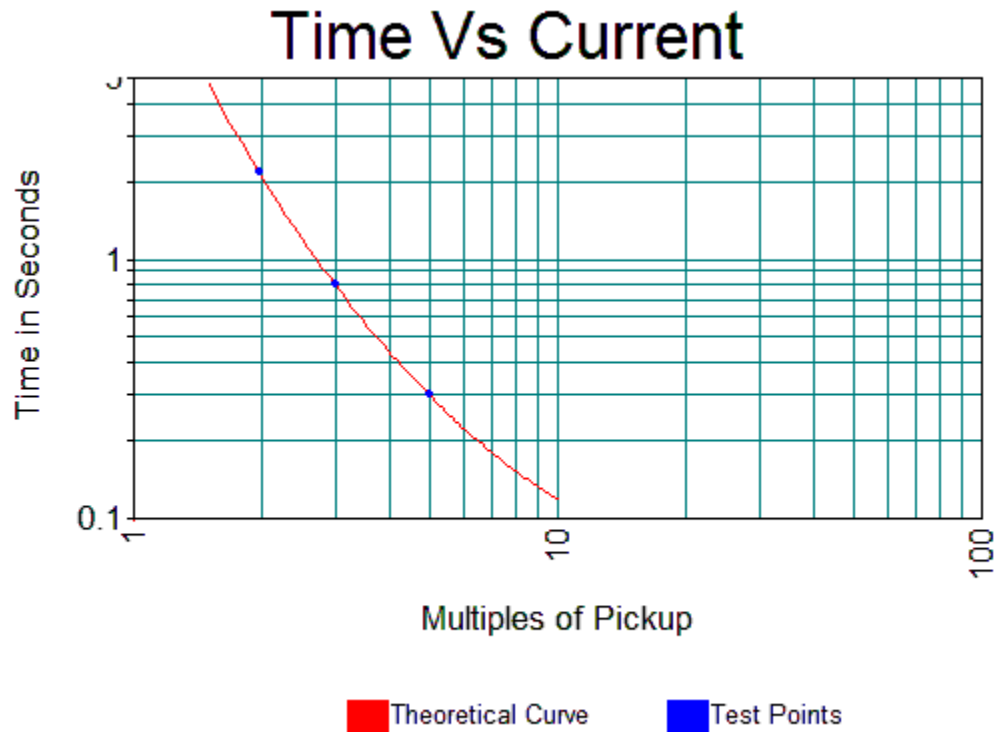

Multiple (X Tap)	Actual Time (Seconds)	Expected Time (Seconds)	Min Range (Seconds)	Max Range (Seconds)	Pass/Fail (Results)
2.00	2.15	2.09	1.99	2.20	Pass
3.00	0.80	0.79	0.75	0.83	Pass
5.00	0.30	0.30	0.28	0.31	Pass

Record of Protective Relay Test Results

Performed By:


CEMIRT

Base:	Dyess AFB TX	Relay:	Multifunction
Substation:	Alpha	Device:	Microprocessor
Feeder:	A2 West Housing	Manufacturer:	GE
Tested By:	Mr. Willet/SSgt Miron	Inst. Bklt:	GEK-86132
Date Tested:	08/24/2016	Relay Test Set:	Megger MPRT 8430

Relay 2: Neutral Pickup Test

Actual Pickup (Amps)	Expected Pickup (Amps)	Min Range (Amps)	Max Range (Amps)	Pass/Fail (Result)
0.75	0.75	0.71	0.80	Pass

Relay 2: Neutral Time Overcurrent Test

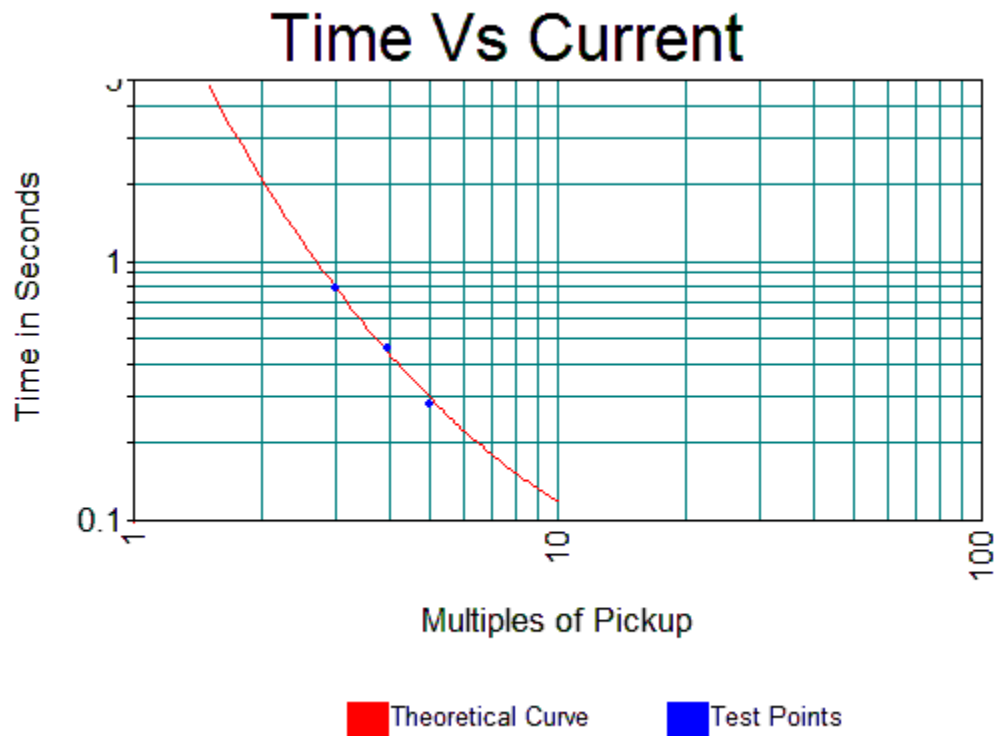

Current Multiple (X Tap)	Actual Time (Seconds)	Expected Time (Seconds)	Min Range (Seconds)	Max Range (Seconds)	Pass/Fail (Results)
3.00	0.78	0.79	0.75	0.83	Pass
4.00	0.46	0.44	0.42	0.46	Pass
5.00	0.28	0.30	0.28	0.31	Pass
